


Id		Nombre de tarea	Duración	Comienzo	Fin	Predecesoras	Nombres de los recursos	octubre							noviembre				diciembre				enero															
								11/09	18/09	25/09	02/10	09/10	16/10	23/10	30/10	06/11	13/11	20/11	27/11	04/12	11/12	18/12	25/12	01/01	08/01	15/01												
1																																						
2		MERCADO PROVISIONAL PARA EL MERCADO CENTRAL LANUZA	87 días?	vie 15/09/17	lun 15/01/18			/09																				15/01										
3																																						
4		C. 1. ACTUACIONES PREVIAS	11 días?	vie 15/09/17	vie 29/09/17			/09																				29/09										
5		C. 2. RED DE SANEAMIENTO	20 días?	lun 09/10/17	vie 03/11/17														03/11																			
6		C. 3. CIMENTACIÓN	20 días	lun 02/10/17	vie 27/10/17														27/10																			
7		C. 4. ESTRUCTURA	23 días?	lun 16/10/17	mié 15/11/17														15/11																			
8		C. 5. ALBAÑILERÍA	11 días?	mié 01/11/17	mié 15/11/17														15/11																			
9		C. 6. CERRAMIENTOS Y DIVISIONES	18 días?	mié 15/11/17	vie 08/12/17														08/12																			
10		C. 7. CUBIERTAS	15 días?	jue 26/10/17	mié 15/11/17														15/11																			
11		C. 8. REVESTIMIENTOS Y FALSOS TECHOS	19 días?	mié 15/11/17	lun 11/12/17														11/12																			
12		C. 9. PAVIMENTOS	16 días?	lun 11/12/17	lun 01/01/18														01/01																			
13		C. 10. CARPINTERIA DE MADERA	5 días?	jue 14/12/17	mié 20/12/17														20/12																			
14		C. 11. CARPINTERIA DE ALUMINIO Y PVC	10 días?	lun 18/12/17	vie 29/12/17														29/12																			
15		C. 12. CERRAJERÍA	15 días?	lun 11/12/17	vie 29/12/17														29/12																			
16		C. 13. VIDRIERÍA	6 días?	mar 02/01/18	mar 09/01/18														09/01																			
17		C. 14. CLIMATIZACIÓN	23 días?	jue 07/12/17	lun 08/01/18														08/01																			
18		C. 15. FRÍO INDUSTRIAL	21 días?	mié 13/12/17	mié 10/01/18														10/01																			
19		C. 16. FONTANERÍA	30 días?	mié 15/11/17	mar 26/12/17														26/12																			
20		C. 17. PROTECCIÓN CONTRA INCENDIOS	22 días?	mar 28/11/17	mié 27/12/17														27/12																			
21		C. 18. ELECTRICIDAD BAJA TENSIÓN	28 días?	mié 22/11/17	vie 29/12/17														29/12																			
22		C. 19. COMUNICACIONES	14 días?	vie 22/12/17	mié 10/01/18														10/01																			
23		C. 20. PINTURAS	43 días?	mié 15/11/17	vie 12/01/18														12/01																			
24		C. 21. VARIOS	11 días?	lun 01/01/18	lun 15/01/18														15/01																			

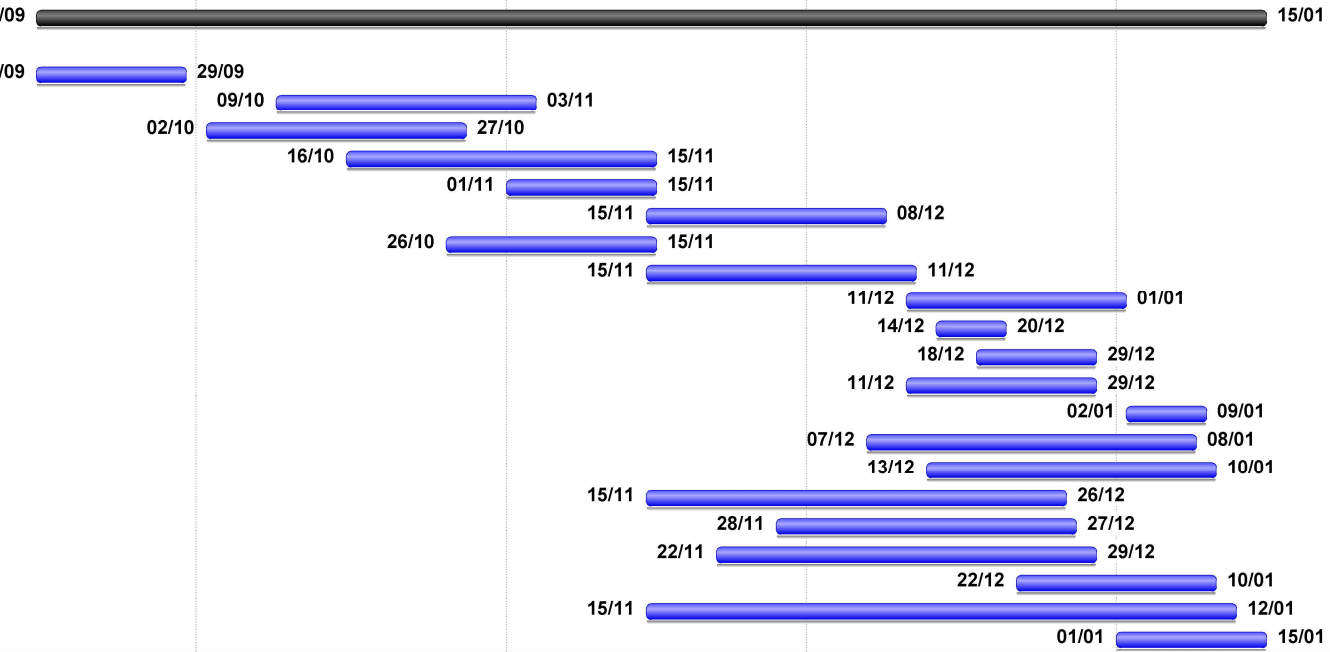

MERCADO PROVISIONAL PARA EL MERCADO CENTRAL LANUZA. PLANNING ECONÓMICO

CAPITULO	IMPORTE TOTAL	15 SEPT(2017)-15 OCT(2017)	16 OCT(2017)-15 NOV(2017)	16 NOV(2017)-15 DIC(2017)	16 DIC(2017)-15 ENE(2018)
C.1. ACTUACIONES PREVIAS	12.449,20 €	12.449,20 €			
C.2. RED DE SANEAMIENTO	23.868,51 €	4.773,70 €	19.094,81 €		
C.3. CIMENTACIÓN	85.039,35 €	42.519,68 €	42.519,68 €		
C.4. ESTRUCTURA	134.716,45 €		134.716,45 €		
C.5. ALBAÑILERÍA	9.279,59 €		9.279,59 €		
C.6. CERRAMIENTOS Y DIVISIONES	101.379,65 €			101.379,65 €	
C.7. CUBIERTAS	46.829,84 €		46.829,84 €		
C.8. REVESTIMIENTOS Y FALSOS TECHO	67.957,06 €			67.957,06 €	
C.9. PAVIMENTOS	15.886,67 €			2.383,00 €	13.503,67 €
C.10. CARPINTERIA DE MADERA	2.475,42 €				2.475,42 €
C.11. CARPINTERIA DE ALUMINIO Y PV	32.101,45 €				32.101,45 €
C.12. CERRAJERÍA	51.538,44 €			10.307,69 €	41.230,75 €
C.13. VIDRIERÍA	5.738,58 €				5.738,58 €
C.14. CLIMATIZACIÓN	51.255,73 €			12.813,93 €	38.441,80 €
C.15. FRÍO INDUSTRIAL	98.855,33 €			14.828,30 €	84.027,03 €
C.16. FONTANERÍA	37.933,14 €			22.759,88 €	15.173,26 €
C.17. PROTECCIÓN CONTRA INCENDI	22.126,11 €			11.063,06 €	11.063,06 €
C.18. ELECTRICIDAD BAJA TENSIÓN	105.811,28 €			42.324,51 €	63.486,77 €
C.19. COMUNICACIONES	23.243,45 €				23.243,45 €
C.20. PINTURAS	25.550,56 €			17.885,39 €	7.665,17 €
C.21. VARIOS	7.691,13 €				7.691,13 €
	PARCIAL	59.742,58 €	252.440,36 €	303.702,47 €	345.841,53 €
	ACUMULADO	59.742,58 €	312.182,94 €	615.885,41 €	961.726,94 €
